

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 1

Item ID: D350-748-201

Accept

N900040100

Setup Start *NS1*

Revision ID:

Stop *NS2*

Item Name: Aft Crosstube

Start Date: 6/30/14 Start Qty: 1.00 *1*

Cust Item ID:

Required Date: 8/11/14 Req'd Qty: 1.00 *1*

Customer:

Reference:

Approvals: Process Plan: WM Date: 7/30/14 Tooling: _____ Date: _____

Run Start *NR1*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D350-748-241	G

Self

MCS 150223

100

Document Control

0.00

DAS

100

DOCUMENT CONTROL

27

DC

Memo

0.00

9-89

Doc.Control -USB or Paperwork

Photocopy bluefile & type labels per PPPD350-748-201

CHG003

FEB 25 2015

110

0.00

110

BENDING MACHINE - CROSSTUBES

CNC Bend 2

Memo

0.00

CNC Alpha 160 Bender

Bend tube as per Dwg D350-748-241 using CNC bender program D350A and Folio FT _____

*****UNDER BEND .225" PER SIDE*****

*****USE (4) DT9824 SHIM BLOC TO CHECK STRAIGHTNESS*****

JWT 11-11-24

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width:100%;"> <tr> <td>Skid-tube ☐</td> <td>Crosstube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>	Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐															
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐															
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐															
Large Fab ☐	Composite ☐	Supplier ☐																

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear	General	Other	Other
☐ Bending	☐ Bend	☐ Folio/Program	☐ Outside Dimensions
☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance
☐ Cracks	☐ Broken/Damage/Defect	☐ Hardware	☐ Part Incorrect
☐ Crimp/Kink/Ripple/Wave	☐ Burrs	☐ Inspection Incomplete/Unqualified	☐ Part Lost/Missing
☐ Cuffs	☐ Contamination	☐ Instructions Incomplete/Unclear	☐ Part Moved
☐ Crushing	☐ Countersink	☐ Misaligned/off center	☐ Positioned Wrong
☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Power Loss/Surge
☐ Inspection Strip in Tube	☐ Drawing	☐ Misread	☐ Pressure/Forced
☐ Marks/Chatter	☐ Drill Holes	☐ Off-set	☐ Set-up
☐ Turning Sequence	☐ Finish	☐ Out of Calibration	☐ Temperature/Cure
☐ Wave/Twist in Tube	☐ Fit/Function	☐ Out of Sequence	☐ Weld
			☐ Wrong Stock Pulled
			☐ Other

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 2

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Item Name: Aft Crosstube

Stop ***NS2***

Start Date: 6/30/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/11/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

120

0.00

120


Crosstubes

Memo

0.00

Crosstubes

VERIFY CROSSTUBE DIMENSIONS AS PER DWG

 14-11-24

125

0.00

125

Outsource1

Memo

0.00

Outsource process - Heat Treat

ISSUE P/O TO METCOR: 26588

Stress relief

Heat treat crosstube as per QSI010 4.3 within 12h after bending

CL 14/11/21 ①

126

Receive & Inspect for Damage & Mat'l Certs

0.00

126

Packaging

Memo

0.00

Packaging

1x SP14-11-26

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 3

Item ID: D350-748-201 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Aft Crosstube
Start Date: 6/30/14 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 8/11/14 Req'd Qty: 1.00 ***1*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

127	QC15- Crosstube Dimensional Check	0.00							
-----	-----------------------------------	------	--	--	--	--	--	--	--

127

QC

Quality Control

Memo

MARK CUT LINES

0.00

DAS 03 9-89  14-11-27

128

128

Crosstubes

Crosstubes

Memo

CUT TUBE AT HEIGHT ON FAI SHEET

VERF HEIGHT 31.56 BY QC 15 LEVEL INSPECTOR

VERF TWIST 0.0 BY QC15 LEVEL INSPECTOR

0.00

DAS 03 9-89  14-11-27

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION ☐ Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved	AGAINST DEPARTMENT/PROCESS ☐ Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 4

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Item Name: Aft Crosstube

Stop ***NS2***Start Date: 6/30/14 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 8/11/14 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start ***NR1***
Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
130	Crosstubes	0.00							
130									
Crosstubes	Memo	0.00							
Crosstubes									
	2- Drill Tube as per Dwg D350-748-241 Using DT8876 Drill Jigs, Set-up drill table as per QSI 010								
	3 -Deburr								
	4- Engrave Part # and Batch # as per Dwg D350-748-241								
	5-Remove all marks from tube within limits of D350-748-241								
140	QC6- Inspect dimensions to drawing	0.00							
140									
QC	Memo	0.00							
Quality Control									

DAS
38
9-89

DEC 09 2014

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 5

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Item Name: Aft Crosstube

Stop ***NS2***Start Date: 6/30/14 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 8/11/14 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start ***NR1***Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150	Outsource process-Cadplate per QSI017 4.1.9.1	0.00							
150									
Outsource3	Memo	0.00							
Outsource process - Cad plate	Issue P/O: <u>26894</u> Stress relief at 375° for 5 hours Magnetic Particle Inspect per ASTM E1444 Cadium Plate per AMS-QQ-P-416B, Class 1, Type 2 Embrittle relief at 375° for 8 hours, Chromate Treat Possible Supplier: Southwest United Industries Ensure Certificate of Conformity is attached								<u>CL 14/12/23 @</u>
160	Receive & Inspect for Damage & Mat'l Certs	0.00							
160									
Packaging	Memo	0.00							
Packaging	Ensure certificate of conformity is attached								<u>1X SP 15-02-10</u>
170	QC5- Inspect part completeness to step on W/O	0.00							
170									
QC	Memo	0.00							
Quality Control									<u>1</u> DAS 38 9-89 <u>15-02-10</u>

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ •Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	---	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 6

Item ID: D350-748-201

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Aft Crosstube

Start Date: 6/30/14

Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/11/14

Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

174

Outsource process - NDT per QSI038 4.1

0.00

174

Outsource2

Memo

0.00

Outsource process - NDT

ISSUE P/O TO ACCUREN:

27400CL 1502/12 ①

176

Receive & Inspect for Damage & Mat'l Certs

0.00

176

Packaging

Memo

0.00

Packaging

IN 801502-12

178

QC5- Inspect part completeness to step on W/O

0.00

178

QC

Memo

0.00

Quality Control

DAS
38
9-89115-02-12

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 7

Item ID: D350-748-201

Accept

N900040100

Setup Start

NS1

Revision ID:

Item Name: Aft Crosstube

Stop

NS2

Start Date: 6/30/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/11/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan:

Date:

Tooling:

Date:

Run Start

NR1

QC:

Date:

SPC (Y/N):

Date:

Stop

NR2

Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Tool ID

Tool #

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

180

180

SprayPaint

Spray Painting

SprayPaint

Memo

1-Prime inside and out crosstube as per QSI 005 4.2

BATCH: M121807

2-Paint Outside of Tube as per Dart QSI 005 4.2

BATCH: 131233

0.00

0.00

* Part changed WAXES From Dupont to ^{ANALTA} ~~AYLATA~~
Sizing (industrial Tech. sheet attached)

DAS
38
9-88

190

190

QC

Quality Control

QC14- Inspect Spray Paint

Memo

Then, Wrap in plastic bag to protect from scratches

0.00

0.00

15-02-23

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube ☐</td> <td>Crosstube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>	Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐															
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐															
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐															
Large Fab ☐	Composite ☐	Supplier ☐																

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 8

Item ID: D350-748-201

Accept

N900040100Setup Start ***NS1***

Revision ID:

Item Name: Aft Crosstube

Stop ***NS2***

Start Date: 6/30/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/11/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
200	Crosstubes	0.00							
200									
Crosstubes	Memo	0.00							
Crosstubes	INSTALL GROUND WIRE INSERT, THEN INSERT SCREW AND WASHER								
	1-Abrade mating surfaces of support and crosstube with 180 grit sandpaper, clean the area with MEK or equivalent as per dwg								
	2-Install supports with Proseal 890 per D350-748-241 and QSI 015								
	A/R Proseal 890 Batch: <u>130 986</u>								
	EXP: <u>6/15</u>								
	3-Install supports clamps Using Dt8876 as per Dwg D350-748-241, Torque to 60-80 IN-LBS.								
	PROSEAL CURE TIME 72 HOURS:								
	Start: <u>15-02-18</u>								
	Finish: <u>15-02-18</u>								
210	QC5- Inspect part completeness to step on W/O	0.00							
210									
QC	Memo	0.00							
Quality Control	***RE-CHECK TORCQUE ON CLAMP AFTER PROSEAL HAS CURED FOR 72HOURS AS PER DWG.***								

DAS
38
9-89

15-02-23

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 9

Item ID: D350-748-201

Accept

N900040100

Setup Start

NS1

Revision ID:

Item Name: Aft Crosstube

Stop

NS2

Start Date: 6/30/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/11/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start

NR1

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
220	Pick Kit	0.00							
220									
Packaging	Memo	0.00				DAS 66 9-89			
Packaging									
									DAS 28 9-89
230	QC4- 100% Inspect kits for completeness	0.00							
230									
QC	Memo	0.00				DAS 27 FEB 25 2015			
Quality Control									
240		0.00							
240									
Packaging	Packaging								
Packaging	Memo	0.00				1X DAS 28 9-89			
Packaging	Identify and pack for shipping as per PPPD350-748-201								FEB 26 2015
	Location: <u>FG 35</u>								
	PPP Rev: _____								

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube ☐</td> <td>Crosstube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>	Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐															
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐															
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐															
Large Fab ☐	Composite ☐	Supplier ☐																

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 122927

Tuesday, July 29, 2014 2:26:09 PM

122927

Page 10

Item ID: D350-748-201

Accept

N900040100

Setup Start

NS1

Revision ID:

Item Name: Aft Crosstube

Stop

NS2

Start Date: 6/30/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 8/11/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run

Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

250

QC21- Final Inspection - Work Order Release

0.00

250

QC

Memo

0.00

Quality Control

MCJ 15-02-27

U 15-02-26

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Tuesday, July 29, 2014 2:26:07 PM

Page 1

Work Order ID: 122927

122927

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube

Start Date: 6/30/14

Required Date: 8/11/14

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP Rev: A New Issue 06-07-05 JLM
 IPP Rev: B Update qty of MS21042L5 06-09-12 KJ
 IPP Rev C Combined manufacturing 08.04.02 EC verified by: DD
 IPP Rev:D 08-06-24 revD as per dwg DD verified by:EC
 IPP Rev: E 08.12.11 Step17 was step 21 KJ Verified by:EC IPP Rev:F
 10.08.04 added QSI010 4.3 DD verf:EC IPP REV:G ADD
 UNDER BEND COMMENT 12-05-28 JLM IPP REV:H 12.11.05 as per
 dwg D350-748-141G DD verf:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

ALS4-1032-225	AELS8-1032-225	Purchased	No			200	Each	417.0000	1	1			
											DAS		
											41		
											9-89	15-2-18	

AI S4-1032-225

Rivnut

Location	Loc Qty	Loc Code
FG	30	
M127028	30	
ST267	387	
M127028	10	
M127092	26	
M128179	338	
M128649	13	

AN4-41A		Purchased	No			220	Each	552.0000	8	8			
											DAS		
											28		
											9-89		

AN4-41A

Bolt

Location	Loc Qty	Loc Code
ST517	552	
124241	2	
124805	365	
124836	185	

DAS
27
9-89

DAS
28
9-89

FEB 24 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Tuesday, July 29, 2014 2:26:07 PM

Page 2

Work Order ID: 122927

122927

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube

Start Date: 6/30/14

Required Date: 8/11/14

Start Qty: 1.00

Required Qty: 1.00

AN4-6A Purchased No 220 Each 2,168.000 16 16

AN4-6A

BOLT

**

DAS

26

9-89

DAS

28

9-89

Location

Loc Qty

Loc Code

ST355

604

16067

4

M128403

600

ST514

1564

M126317

350

M128634

1214

16

DAS

26

9-89

AN5-32A

Purchased No

220 Each

339.0000

4

4

AN5-32A

Bolt

**

130716

DAS

28

9-89

Location

Loc Qty

Loc Code

ST336

339

124215

89

m127363

4

m127550

30

m128403

66

m128634

150

D3500-1

Manufactured No

220

Each

65.0000

4

4

D3500-1

Saddle

**

121516

DAS

26

9-89

Location

Loc Qty

Loc Code

ST406

65

108799

1

115746

40

120311

24

FEB 24 2015

DAS

28

9-89

DAS

27

9-89

Tuesday, July 29, 2014 2:26:08 PM

Shop Packet Print

Page 2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Tuesday, July 29, 2014 2:26:08 PM

Page 3

Work Order ID: 122927

122927

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube

Start Date: 6/30/14

Required Date: 8/11/14

Start Qty: 1.00

Required Qty: 1.00

D3501-1

Manufactured No

220

Each

922.0000

16

16

D3501-1

Bushing

**

6

DAS

9-89

9-89

DAS

28

9-89

FEB 24 2015

DAS
27
9-89

Location

Loc Qty

Loc Code

ST046

922

119012

252

119635

178

120509

240

121132

70

121654

120

121859

60

86913

2

16

D3502-1

Manufactured No

200

Each

109.0000

2

2

D3502-1

Support

**

CR 15-02-2014

Location

Loc Qty

Loc Code

LG050

109

104334

6

110283

13

110785

8

113181

2

114329

12

119578

12

121096

12

94722

20

97212

12

99764

12

2

Tuesday, July 29, 2014 2:26:08 PM

Shop Packet Print

Page 3

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Skid-tube ☐ Crosstube ☐ Water Jet ☐ Engineering ☐ Scrap ☐ Machining ☐ Small Fab ☐ Prod. Eng. Coord. ☐ Quality ☐ Use-as-is ☐ Thermoforming ☐ Finishing ☐ Rec/Store/Packaging ☐ Other ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Large Fab ☐ Composite ☐ Supplier ☐
--	--	--

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Tuesday, July 29, 2014 2:26:08 PM

Page 5

Work Order ID: 122927

122927

Parent Item: D350-748-201

D350-748-201

Parent Item Name: Aft Crosstube

Start Date: 6/30/14

Required Date: 8/11/14

Start Qty: 1.00

Required Qty: 1.00

MS21042L4

Purchased

No

220

Each

4,073.000

24

24

MS21042L 4

Locknut

**

131618

DAS

28

9-89

DAS

28

9-89

DAS
27
9-89

Location

Loc Qty

Loc Code

ST307

4073

126275

5

m126015

12

m126275

27

m127255

63

m127376

11

m127813

891

m128300

80

m128798

1984

m129472

1000

MS21042L5

Purchased

No

220

Each

950.0000

4

4

MS21042L 5

Nut

**

131340

DAS

28

9-89

DAS
27
9-89

Location

Loc Qty

Loc Code

ST307

950

117611

1

125684

8

m127304

1

m127813

500

m128810

7

m129472

433

MS21920-22

Purchased

No

200

Each

214.0000

2

2

MS21920-22

Clamp

**

15-02-20

Location

Loc Qty

Loc Code

LG050

214

M127255

14

M128636

200

Tuesday, July 29, 2014 2:26:08 PM

Shop Packet Print

Page 5

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Tuesday, July 29, 2014 2:26:08 PM

Page 6

Work Order ID: 122927

Parent Item: D350-748-201

Parent Item Name: Aft Crosstube

122927

D350-748-201

Start Date: 6/30/14

Required Date: 8/11/14

Start Qty: 1.00

Required Qty: 1.00

MS27039-1-10

Purchased

No

200

Each

872.0000

1

1

DAS

41

9-89

15-2-18

MS27039-1-10

SCREW

130358

Location

Loc Qty

Loc Code

ST290

872

m126474

1

m128401

39

m128635

582

m129541

250

NAS1149D0363J

Purchased

No

200

Each

2,574.000

1

1

DAS

41

9-89

15-2-18

NAS1149D0363.J

Washer

Location

Loc Qty

Loc Code

GA

23

124392

23

ST276

8

m123441

8

ST510a

2543

m126319

2

m128429

2541

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Tuesday, July 29, 2014 2:26:08 PM

Page 7

Work Order ID: 122927

Parent Item: D350-748-201

Parent Item Name: Aft Crosstube

122927

D350-748-201

Start Date: 6/30/14

Required Date: 8/11/14

Start Qty: 1.00

Required Qty: 1.00

NAS1149D0463J

Purchased

No

220

Each

7,118.000

32

32

DAS

05

9-89

NAS1149D0463.J

WASHER

DAS
28
9-89

Location

Loc Qty

Loc Code

CA

485

M129682

485

ST277

6633

16941

8

M126221

20

M127813

6

M127904

127

M128591

45

M128995

1500

M129390

4927

FEB 25 2015

DAS
27
9-89

32

NAS1149D0563J

Purchased

No

220

Each

2,403.000

8

8

NAS1149D0563.J

Washer

13/02/6

DAS
28
9-89

Location

Loc Qty

Loc Code

GA

129

m125807

129

ST510a

2274

m126319

282

m128257

1992

DAS

05

9-89

DAS
27
9-89

FEB 25 2015

Tuesday, July 29, 2014 2:26:09 PM

Shop Packet Print

Page 7

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube ☐</td> <td>Crosstube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>	Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐															
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐															
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐															
Large Fab ☐	Composite ☐	Supplier ☐																

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Item	Qty	Part Number	Description
1	X	D350-748-241	CROSSTUBE ASSEMBLY (AS 350/355 HI AFT)
2	1	D6015-125	CROSSTUBE (OR D6018-125)
3	2	D3502-1	SUPPORT
4	2	D3595-063-395	RUBBER CUSHION
5	1	AELS-1032-225	INSERT
6	1	NAS1149D0363J	WASHER (OR AN960JD10)
7	2	MS21920-22 OR MS21920-21	CLAMP (PER DART SPEC. M-MS21920-21/-22)
8	1	MS27039-1-10	SCREW
9	A/R	PROSEAL 890 B-2	SEALANT, AMS-S-8802 CLASS B-2

GENERAL NOTES:

- 1) MATERIAL: MANUFACTURED FROM D6015-125 OR D6018-125
FINISHED LENGTH AFTER TURNING = 124.70±0.06 (AFTER BENDING/TRIMMING = 122.70 REF)
- 2) FINISH: MAGNETIC PARTICLE INSPECT PER DART QSI 038 4.2
CADMIUM PLATE PER AMS-QQ-P-416B, CLASS 1, TYPE II
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 3) TOLERANCE: PER DART QSI 018 UNLESS OTHERWISE NOTED.
WALL THICKNESS ECCENTRICITY PER DART QSI 038 7.2
MIN. ALLOWABLE WALL IS -0.020 FROM NOMINAL
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED.
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX.
- 6) IDENTIFICATION: DART PART NUMBER "D350-748-241" AND BATCH NUMBER ON INSIDE OF CUFF
PER DART QSI 044 6.4 (VIBRATING STYLUS)
- 7) WEIGHT: 29.85 lbs
- 8) PART IS SYMMETRIC ABOUT CENTERLINE, EXCEPT FOR Ø0.297 HOLE.
- 9) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.

TURNING

- 10) BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- 11) HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 OR AMS2759/1E AFTER TURNING. ACCEPTABLE TO VERIFY TENSILE STRENGTH BY HARDNESS TEST PER ASTM E18 TO 40-45 HRC.

BENDING

- 12) ALL DIMENSIONS FOR BENT TUBE ARE POST STRESS RELIEF
- 13) BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES PER SIDE. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 8% BASED ON O.D. ON TOP HALF OF BEND, AND 7% ON BOTTOM HALF OF BEND.
- 14) MAX AMPLITUDE OF RIPPLING ALONG BENT PORTION OF THE TUBE IS 0.030 (ZN A1-3)
- 15) AFTER BENDING, STRESS RELIEVE TUBE AT 650°F ±0.25°F FOR A MINIMUM OF 2 HRS AND ALLOW TO COOL TO AMBIENT TEMPERATURE (REF AMS2759/1E).
- 16) MAX TWIST AFTER STRESS RELIEF: WITH XTUBE LAYED FLAT ON SURFACE, THE DIFFERENCE BETWEEN CUFF HEIGHTS FROM THE SURFACE MAY BE NO LARGER THAN 0.38 (ZN C1-3).

ASSEMBLY

- 17) TO INSTALL D3502-1 SUPPORT: ABRASE MATING SURFACE OF SUPPORT AND CROSSTUBE WITH 180-GRIT SANDPAPER AND REMOVE RESIDUE WITH MEK (OR EQUIVALENT). APPLY A 0.02" TO 0.05" THICK LAYER OF PROSEAL 890 CLASS B-2 (OR AMS-S-8802 CLASS B-2) SEALANT TO MATING SURFACE OF SUPPORT.
- 18) TORQUE CLAMPS 60 TO 80 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING. PRIOR TO PACKAGING, RE-CHECK TORQUE ON CLAMPS AFTER PROSEAL 890 SEALANT HAS CURED FOR 72 HOURS.


SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 122927
7/30/14 WSM

RELEASE
2012-11-03


G	RMV ABRASION STRIP, SUPPORT NOW W/ PROSEAL & CUSHION, ADD STRESS RELIEF, LONGER CUFF, NOW TRIMD AFTER BEND, ADD WALL DIMS & UPDATE TOL.	CP	12.09.12
F	ADD HRC TEST OPTION (B8-1) PER PAR 09-040, ADD TWIST LIMIT (A8-1, C1-3), ADD D6015-125 OPTION (C8-1), STOCK DIM NOW MACHINED (D1-4)	CP	10.11.23
E	REVISE GENERAL NOTES; UPDATE TO CURRENT STANDARDS; RELOCATED FLAG #6 PER PAR 08-046 (ZN A8-3); ADD TOLERANCES (ZN C8-3, D2-3)	RF	09.09.30
D	MAG. PARTICLE AND CAD PLATE AS MFD.	CP	06.10.31
C	ADD CAD PLATING	CP	06.08.14
B	ADD D6018-125 & PRIME AND PAINT	CP	06.06.30
A	NEW ISSUE	CP	06.03.31
REV.	DESCRIPTION	BY	DATE
DESIGN			
DRAWN			
CHECKED			
MFG. APPR.			
APPROVED			
DE APPR.			
DATE	12.09.12		

DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWING NO. D350-748-241	REV. G SHEET 1 OF 4
TITLE CROSSTUBE (AS 350/355 HI AFT)	SCALE NTS
COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

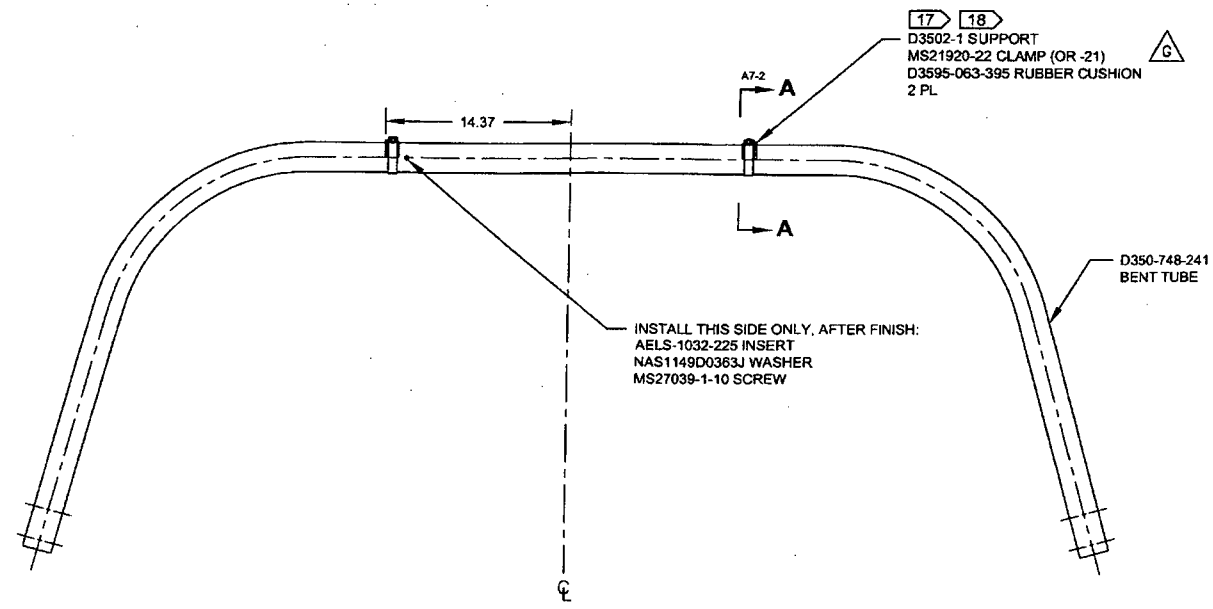

**D350-748-241
ASSEMBLY DETAIL**

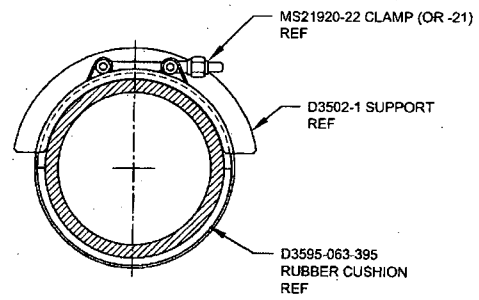



SECTION A-A D4-2
SCALE 6X

RELEASED
2012-11-01

DESIGN	92	DART AEROSPACE LTD	
DRAWN	92	HAWKESBURY, ONTARIO, CANADA	
CHECKED	AV	DRAWING NO.	REV. G
MFG. APPR.	AV	D350-748-241	SHEET 2 OF 4
APPROVED	AV	TITLE	SCALE
DE APPR.	AV	CROSSTUBE (AS 350/355 HI AFT)	NTS
DATE	12.09.12	COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	


8 7 6 5 4 3 2 1

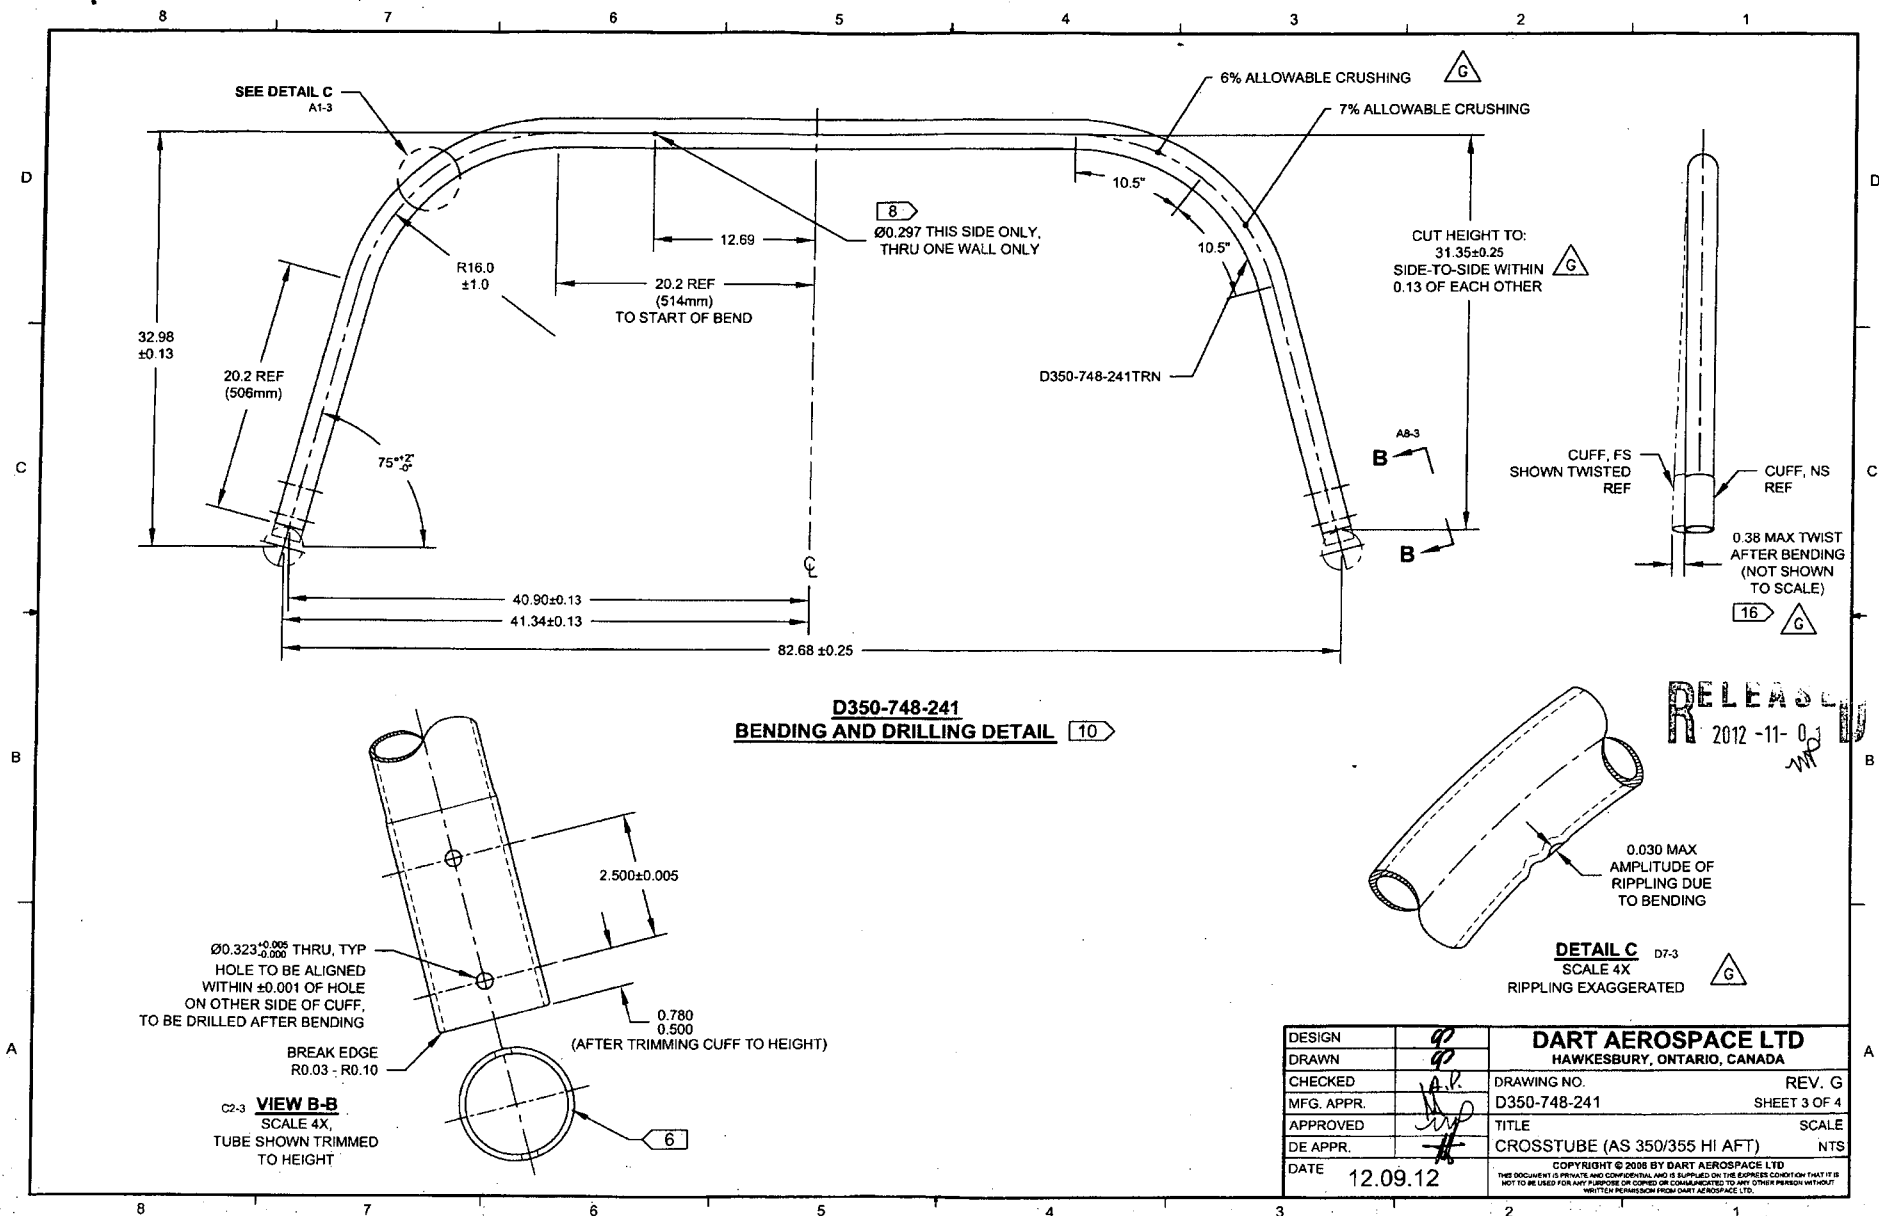

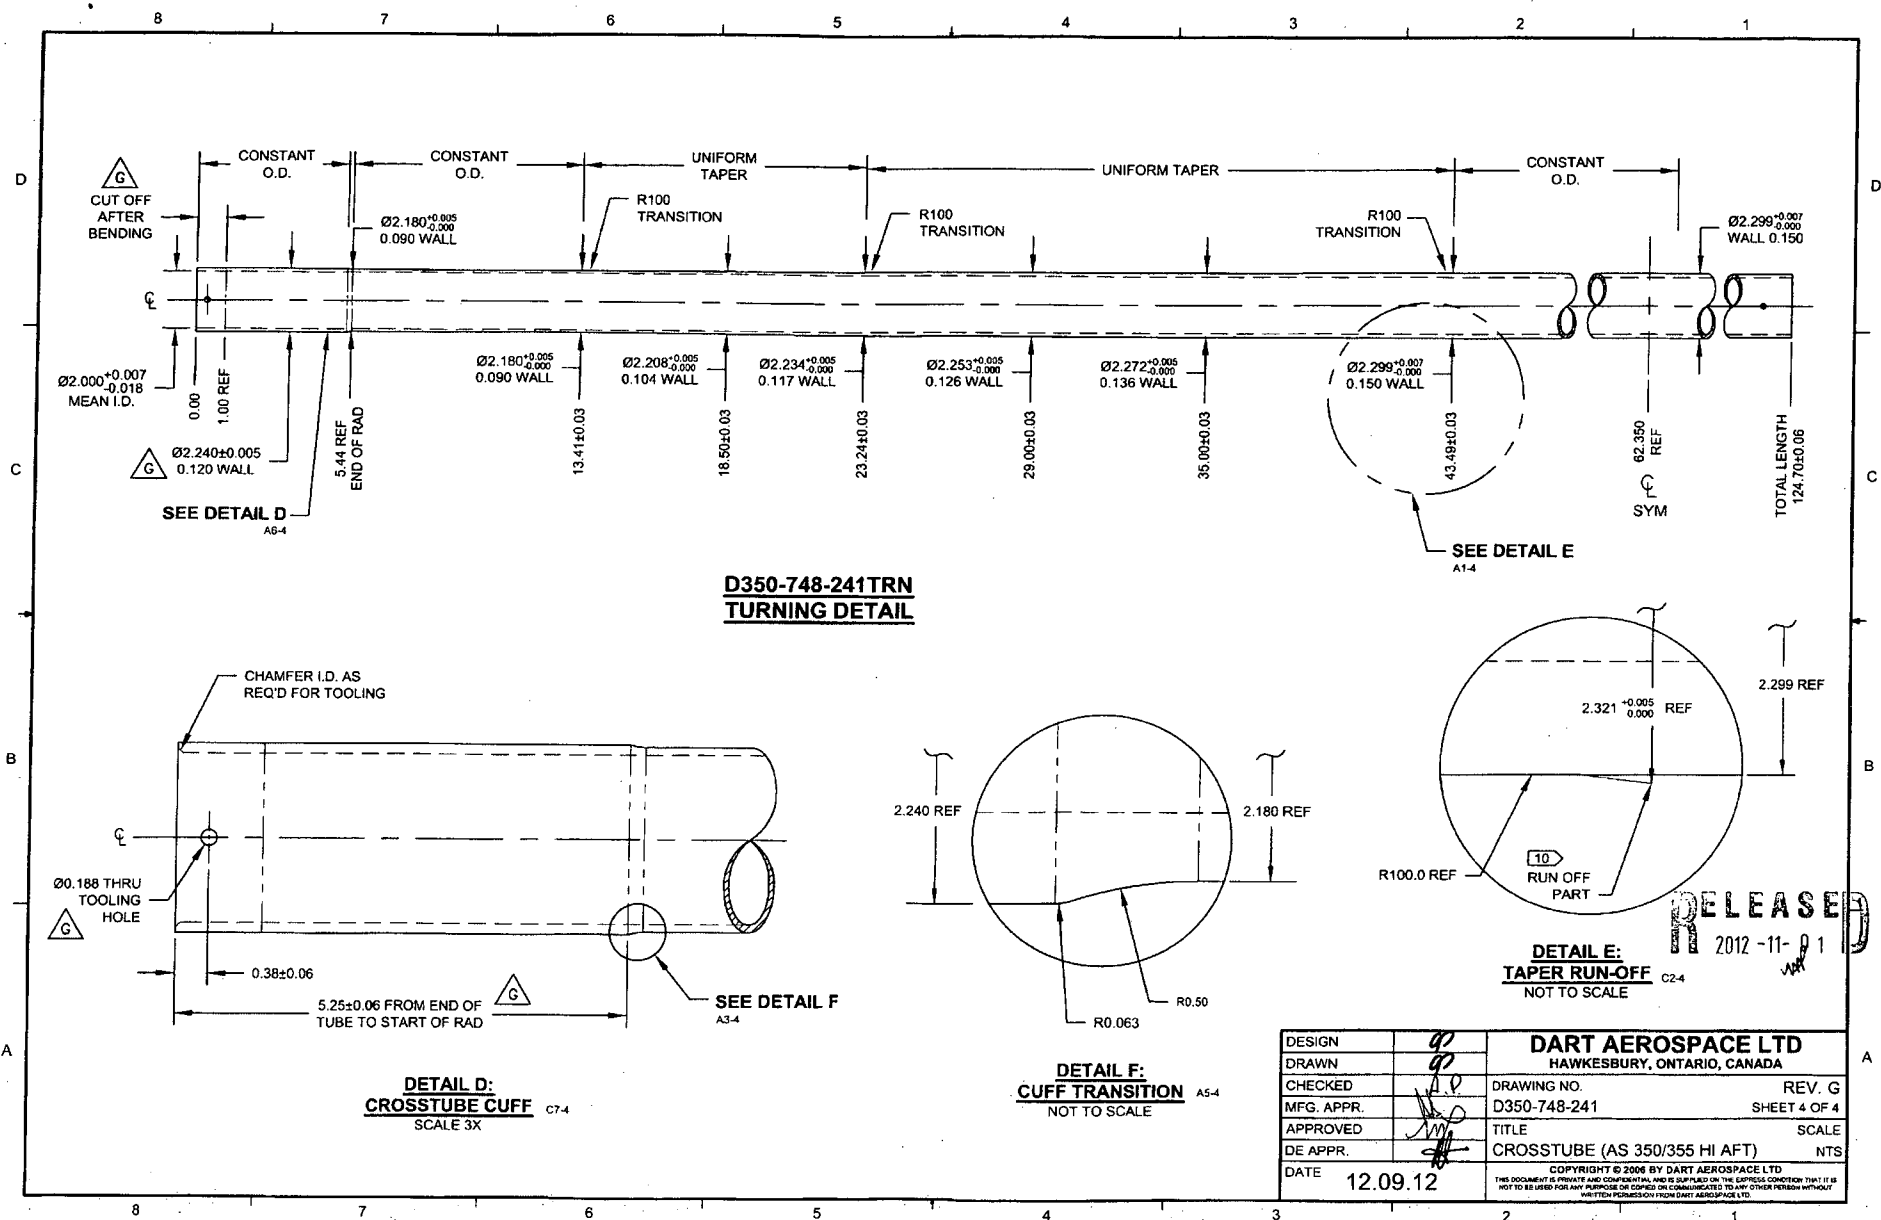

DART AEROSPACE LTD	Work Order:	
Description: Crosstube High Aft (AS350/355)	Part Number:	D350-748-201
Inspection Dwg: D350-748-241 Rev: G		Page 1 of 1

Required Dimension	Min	Max
Height	31.10	31.60
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.54	82.06
Bending Passes	7	--
Crushing	--	7%
Twist	--	0.38

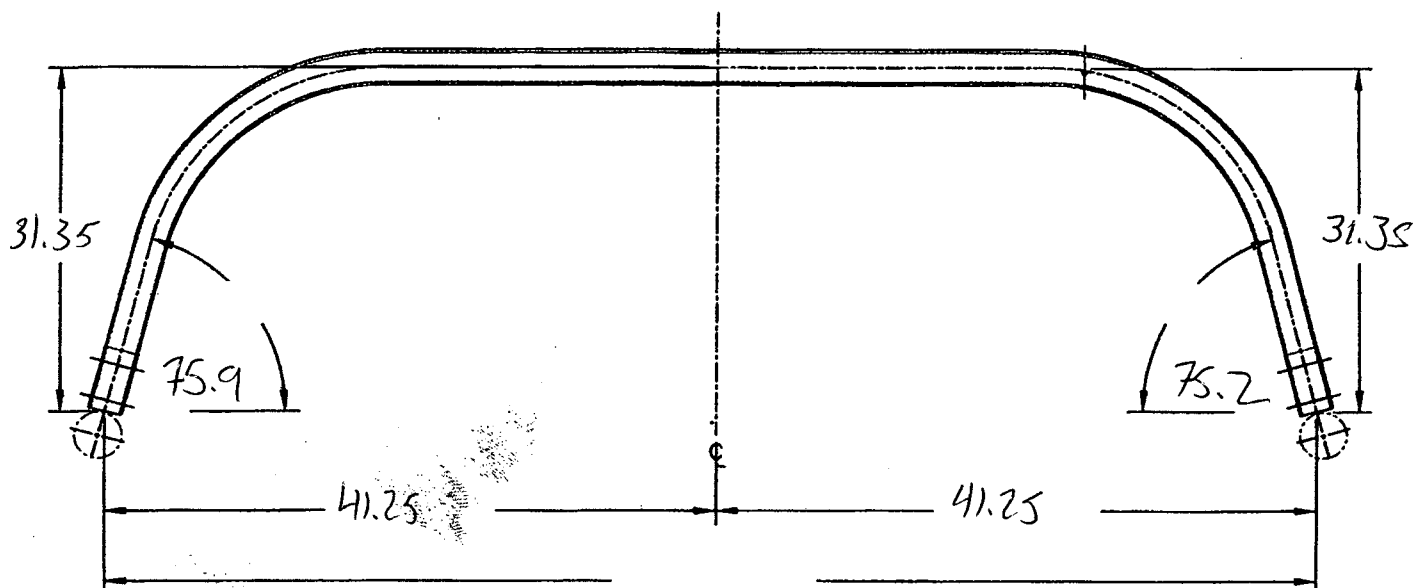

	Side A	Side B
Bending Passes	40	40
Crushing		
Comments		
Twist = 0.000"		

QC15 Inspection	
Date	

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	
C	12.04.16	Added bending, crushing & twist dimensions	KJ	
D	12.07.31	Dwg Rev updated	KJ	
E	13.02.27	Dwg Rev updated	KJ	
F	14.02.13	Crushing & twist dimensions revised	KJ	
G	14.11.10	Height dimension revised	KJ	



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO26588**

Purchase Order Date 11/21/2014

PO Print Date 11/25/2014

Page Number 2 of 3

From :

VC-MET004

Ship To : DART AEROSPACE LTD

ETCOR INC.
50 BOUL. ARTHUR SAUVE
SAINT-EUSTACHE, QC J7R 5A8
CA

1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone 450 473 1884

Ship To Contact

Ship To Phone

Ship Via: Dart Truck

Ship Acct:

Buyer

Chantal Lavoie

Customer POID

Customer Tax # 10127-2607

Terms Net 30

Currency CAD

FOB FCA - (Free Carrier)

122927

D350-748-201
CROSSTUBE

11/25/2014

1.00

\$203.00

\$203.00

Yes

11/25/2014

HEAT TREAT CROSSTUBE AS PER QSI010 4.3
WITHIN 12H AFTER BENDING

SP14-11-26.

Line Total:

\$203.00

122532

D350-748-201
CROSSTUBE

11/25/2014

1.00

\$203.00

\$203.00

Yes

11/25/2014

HEAT TREAT CROSSTUBE AS PER QSI010 4.3
WITHIN 12H AFTER BENDING

Line Total:

\$203.00

Note:

11/25/2014

METCOR INC.

560 BOUL. ARTHUR SAUVÉ
ST-EUSTACHE, QC J7R 5A8
Tel: 450-473-1884 / Fax: 450-491-5498

Recu de livraison

Delivery Receipt

BON DE TRAVAIL	EXPÉDITEUR	BON D'EXPÉDITION
Order	Shipper ID	Shipper
200790	1	86525

EXPÉDITION COMPLETE / Shipped Complete

CLIENT / Customer 215

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
Ph: 613-632-5200
Fax: 613-632-1053



LIVRÉ À / Shipped To

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
Ph: 613-632-5200
Fax: 613-632-1053

COMMANDE DU CLIENT	BON DE LIVRAISON DU CLIENT	TYPE DE MATÉRIEL	DATE DE LA COMMANDE	TRANSPORTEUR
Customer PO	Customer Shipper No.	Material Type	Order Date	Carrier
26588		D2	2014/11/24	client

QUANTITÉ	No. PIÈCE	NOM DE LA PIÈCE	DESCRIPTION DE LA PIÈCE	POIDS
Quantity	Part No.	Part Name	Part Description	Weight

4 D350-748-101

CROSSTUBE

(1) D350-748-201 120198

(1) D350-748-201 122269

(1) D350-748-201 122927 ✓

(1) D350-748-201 122531

1 NIL

170,

SP14-11-24.

TYPE DE CONTENEUR	# DE CONTENEURS	COMMENTAIRES CONTENEUR
Container Type	# Of Containers	Container Comments

NIL

1

CERTIFICAT

EMPAQUETAGE Packing	
------------------------	--

QUANTITÉ EXPÉDIÉE / Quantity Shipped : 4

POIDS EXPÉDIÉ / Weight Shipped : 170,00

QUANTITÉ RESTANTE / Quantity Remaining : 0

POIDS RESTANT / Weight Remaining : 0,00

CERTIFICAT

QUANTITÉ EXPÉDIÉE / Quantity Shipped : 4

POIDS EXPÉDIÉ / Weight Shipped : 170,00

Signature:

Date:

METCOR INC.

560 BOUL. ARTHUR-SAUVÉ, ST-EUSTACHE, QC, J7R 5A8

Tél.: 450-473-1884

Télécopieur / Fax administration: 450-491-5498

Télécopieur / Fax production: 450 491-6454

Certificat de Conformité Détaillé

Detailed Certificate of Compliance

BON DE TRAVAIL order	CHARGEMENT load
200790	1

CLIENT / customer 215

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

COMMANDE DU CLIENT customer po	BON DE LIVRAISON DU CLIENT customer shipper no.	MATÉRIEL material	MAÎTRE D'OEUVRE prime contractor	PROGRAM
26588		Steel		

SPÉCIFICATIONS DU PROCÉDÉ

processing specifications

STRESS REL

SAE AMS 2759/1 REV.E

EXIGENCE / requirement SPÉCIFICATIONS / specified TESTS EXÉCUTÉS / performed RÉSULTATS DE TESTS / results

Visual

QUANTITÉ quantity	POIDS weight	DESCRIPTION DES PIÈCES parts description
4	170	D350-748-101 CROSSTUBE (1) D350-748-201 120198 (1) D350-748-201 122269 (1) D350-748-201 122927 ✓ (1) D350-748-201 122531 1 NIL

SP14-11-24

COMMENTAIRES / comments

STRESS RELIEF 343C, 2 HRS

Le traitement thermique (TT) a été fait en utilisant des équipements en conformité avec AMS2759.

Le TT a été fait tel que requis par AMS2759 et toutes les vérifications et les tests demandés ont été faites et documentés.

Aucun changement n'a été faite par rapport au TT. On certifie que le matériel a été fabriqué, échantillonné, testé et inspecté en accord avec AMS2759 et le bon de commande et le matériel rencontre les exigences spécifiées.

Heat treatment (HT) was performed with equipment that meets the requirements of AMS2759.

All HT operations were in compliance with AMS2759 and all verifications have been performed and documented. No unauthorized changes were performed in regards to the HT. We certify that the material was manufactured, sampled, tested and inspected in accordance with AMS2759 and the purchase order and was found to meet the requirements.

APPROUVÉ par / Approved by:

Isabel Otero


Isabel Otero
QA Technician



DATE: 2014-11-25

DART AEROSPACE LTD		Work Order:	
Description: Crosstube High Aft (AS350/355)		Part Number:	D350-748-241
Inspection Dwg: D350-748-241 Rev: G			Page 1 of 1

Required Dimension	Min	Max
Height	31.10	31.60
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.54	82.06
Bending Passes	7	--
Crushing	--	7%
Twist	--	0.38

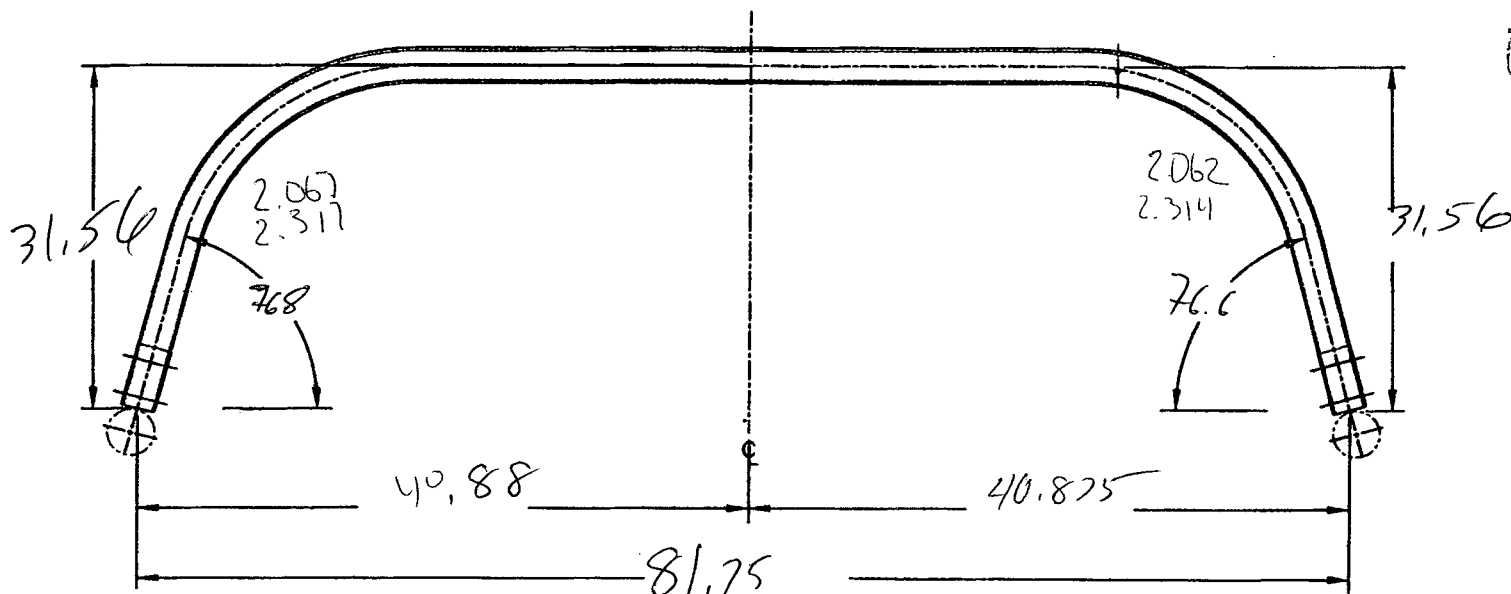

	Side A	Side B
Bending Passes	40	40
Crushing	5.17%	5.18%
Comments		

QC15 Inspection	<i>[Signature]</i> DAS 03 2-09
Date	14-11-27

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	
C	12.04.16	Added bending, crushing & twist dimensions	KJ	
D	12.07.31	Dwg Rev updated	KJ	
E	13.02.27	Dwg Rev updated	KJ	
F	14.02.13	Crushing & twist dimensions revised	KJ	
G	14.11.10	Height dimension revised	KJ	<i>[Signature]</i>



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID PO26894

Purchase Order Date 12/23/2014

PO Print Date 12/23/2014

Page Number 5 of 5

Order From :

CADORATH COATING
2150 LOGAN AVE.
WINNIPEG, MB R2R 0J2
CA

VC-CAD002

Ship To : DART AEROSPACE LTD

1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone 204 633 9420

Ship To Contact

Ship To Phone

Ship Via: Day & Ross collect

Ship Acct:

Buyer

Chantal Lavoie

Customer POID

Customer Tax # 10127-2607

Terms Net 30

Currency CAD

FOB Destination-Collect

12	122927	D350-748-201 CROSSTUBE	1/23/2015	1.00	✓	\$803.42	\$803.42
----	--------	---------------------------	-----------	------	---	----------	----------

Yes

1/23/2015

AS ABOVE

SP15-02-10

Line Total: \$803.42

13	71401-45	PROCUREMENT QUALITY CLAUSES	1/23/2015	1.00		\$0.00	\$0.00
----	----------	--------------------------------	-----------	------	--	--------	--------

No

1/23/2015

Procurement Quality Clauses
A005 right of entry
A012 chemical and physical test report
A021 dart aerospace processing
A024 process certifications
A026 certification of material conformance
A043 retention of quality documents

Line Total: \$0.00

PO Total: \$9,641.04

u cd

Note: Terms & Condition of Purchasing(Suppliers) and Procurement Quality Clauses are an integral part of our AS9100 requirements. To learn in detail, please visit www.dartaerospace.com for further explanation.

Change Nbr: 1

Change Date: 12/23/2014

Packing Slip



Cadorth Coating

2150 Logan Avenue, Winnipeg, Manitoba R2R-0J2

Phone: (204) 633-9420 Fax: (204) 633-8033

INVOICE NUMBER:

S75044

Net 2% Interest Per Month charged on Overdue Accounts.

Any claims for shortages, overcharges, or damaged goods must be made within seven (7) days from receipt of goods.

Sold To:

Dart Aerospace Ltd.
1270 Aberdeen St.

Hawksbury, ON K6A 1K7

ShipTo:

Customer Order #:	DateReceived:	Terms:	G.S.T. #:	Ship Via:	Ship Date:
26894	Jan-19-2015	NET 30 DAYS	10071 6547 RT0001		Feb-05-2015

Item # Qty P/N & Description

1	1 EA	CROSSTUBE	S/N 116923
		P/N d350-748-101	W/O 143069
2	1 EA	CROSSTUBE	S/N 119449
		P/N d350-748-101	W/O 143070
3	1 EA	CROSSTUBE	S/N 120274
		P/N d350-748-101	W/O 143071
4	1 EA	CROSSTUBE	S/N 120281
		P/N d350-748-101	W/O 143072
5	1 EA	CROSSTUBE	S/N 118880
		P/N D350-748-201	W/O 143073
6	1 EA	CROSSTUBE	S/N 118881
		P/N D350-748-201	W/O 143074
7	1 EA	CROSSTUBE	S/N 120198
		P/N D350-748-201	W/O 143075
8	1 EA	CROSSTUBE	S/N 120199
		P/N D350-748-201	W/O 143076
9	1 EA	CROSSTUBE	S/N 120200
		P/N D350-748-201	W/O 143077
10	1 EA	CROSSTUBE	S/N 122531
		P/N D350-748-201	W/O 143078
11	1 EA	CROSSTUBE	S/N 122532
		P/N D350-748-201	W/O 143079
12	1 EA	CROSSTUBE	S/N 122927
		P/N D350-748-201	W/O 143080

SP 15-02-10

**CERTIFICATE OF
CONFORMANCE**

**CADORATH PLATING CO. LTD.
2150 LOGAN AVENUE
WINNIPEG, MANITOBA R2J-0J1**

DATE: Feb-05-2015

CONSIGNED TO: Dart Aerospace Ltd.
1270 Aberdeen St.
Hawksbury, ON K6A 1K7

W/O #: 143080

INVOICE #: 75044

**CONTRACT OR
PURCHASE ORDER #** 26894

DESCRIPTION: CROSSTUBE

QTY 1

P/N # D350-748-201 ✓


S/N # 122927

STRESS RELIEF BAKE HEAT CHART # 15-41.MPI IAW ASTM-E-1444.
CADMIUM PLATE IAW AMS-QQ-P-416C TYPE 2 YELLOW CLASS 1.
FINAL MPI IAW ASTM-E-1444. EMBRITTLE RELIEF BAKE HEAT
CHART # 15-86.

SP 15-02-10

CERTIFICATE: I certify that the items indicated here on have
been inspected and tested and conform to all specifications
and requirements detailed on the contract or purchase order.

Approved Inspector:





Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO27400**

Purchase Order Date 2/11/2015

PO Print Date 2/12/2015

Page Number 4 of 6

Order From :

VC-SKY001

Ship To : DART AEROSPACE LTD

SKYSERVICE
6120 MIDFIELD ROAD
MISSISSAUGA, ONTARIO L5P 1B1
CANADA

1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone 905-678-5636

Ship To Contact

Ship To Phone

Ship Via: Delivered

Ship Acct:

Buyer

Chantal Lavoie

Customer POID

Customer Tax # 10127-2607

Terms

Net 30

Currency

CAD

FOB

FCA - (Free Carrier)

9	122532	D350-748-201 CROSSTUBE	2/12/2015	1.00	\$104.50	\$104.50
---	--------	---------------------------	-----------	------	----------	----------

Yes

2/12/2015

AS ABOVE

Line Total: \$104.50

10	122927	D350-748-201 CROSSTUBE	2/12/2015	1.00	\$104.50	\$104.50
----	--------	---------------------------	-----------	------	----------	----------

Yes

2/12/2015

AS ABOVE

Line Total: \$104.50

11	118880	D350-748-201 CROSSTUBE	2/12/2015	1.00	\$104.50	\$104.50
----	--------	---------------------------	-----------	------	----------	----------

Yes

2/12/2015

AS ABOVE

Line Total: \$104.50

Note:

2/12/2015

**skyservice****Work Order Traveler**
Sky Service F.B.O. Inc.

DOT APP 53-89 / EASA 145.7142 / BDA AMO 385

WO #: MWO23614	Customer: Dart Aerospace Ltd.	Dept: NDT YUL	Reference: 27400
Descr:	PN:	S/N:	Qty: 1
Make:	Model:	Reg:	A/C S/N:
TSN:	CSN:	TSO:	
Task: UNSCHEDULED			Sequence: 1

Work Required:


CARRY OUT NDT ON 13 CROSSTUBES AND 1 FUEL TANK ASSY

1 FUEL TANK ASSY: ITEM ID# D4464-041, W/O ID# 129347
5 FWD CROSSTUBES: ITEM ID# D350-748-101, W/O ID# 122288, 116923, 119449, 120274, 120281,
8 AFT CROSSTUBES: ITEM ID# D350-748-201, W/O ID# 122531, 122532, 122927, 118880, 118881, 120198, 120199, 120200, _____

Action Taken:	Date:	Initial/Stamp:
LIQUID PENETRANT C/O ON ITEMS LISTED ABOVE AS PER ASTM E-1417M-13	FEB 11 2015	
CRACK FOUND ON FUEL TANK ASSY INDICATED ON THE TANK		
REMAINING ITEMS: NO CRACK FOUND		
ARDROX 970P25E BATCH# 2312131, M-20141	FEB 11 2015	

Description	Location	P/N	Qty	Batch	S/N Off	S/N On
		DAS				
		32				
		9-89				

I certified that the maintenance described above has been performed in accordance with the applicable standard of airworthiness.

Signature: 	ACA/SCA Stamp 	Date: FEB 11 2015
Name: RAFIK MELIKIAN		



Imron® 3.5 HG + High Gloss Polyurethane Topcoat (RH Quality)



GENERAL

DESCRIPTION

A high gloss 3.5 lbs/gal VOC conforming, low HAPS, polyurethane topcoat based upon unique Axalta formulations and resin technology. The resulting finish product provides a brush, roll or sprayable topcoat designed for use in any environment where long term color and gloss retention are desired.

SUGGESTED USES

As a high performance topcoat over suitable primers or properly prepared steel, galvanized steel, stainless steel, aluminum, concrete, concrete block, fiberglass, plastics and wood where:

- Long term color retention is desired
- Long term gloss retention is desired
- Compliance with 3.5 lbs VOC regulations is desired
- Use in corrosive or industrial marine environments is needed
- Application by brush, roll or spray is desired
- Excellent chemical resistance is desired
- Outstanding flexibility is needed
- Faster dry times are desired

COMPATIBILITY WITH OTHER COATINGS

- Aged Imron 3.5 HG + may be re-coated with itself following washing with clean, fresh water – no mechanical surface preparation is required.
- Imron 3.5 HG + can be applied over other Axalta coatings including, but not limited to Imron Industrial Strength primers and other Imron primers, Imron waterborne polyurethane copolymer coatings, Corlar® epoxies, Tufcote® acrylics, and Tufcote alkyd primers.
- Imron 3.5 HG + may be used over most aged and hard-cured coatings in good condition. Testing for lifting, bubbling and adhesion is recommended to assure compatibility with unknown coatings. Contact your Axalta representative for specific recommendations.

NOT RECOMMENDED FOR

Immersion service or floors

PERFORMANCE PROPERTIES

Abrasion & Mechanical	Excellent
Alkalis	Excellent
Humidity	Excellent
Solvents	Excellent
Color & Gloss Retention	Excellent
Acids	Excellent
Salts	Excellent
Weather	Excellent

The products referenced herein may not be sold in your market. Please consult your distributor for product availability.

COLOR

Imron 3.5 HG + consists of a mixing system utilizing 19 tints and 1 binder (3500P™) to specific mixing formulas. Select high-volume factory package colors are also available. Thousands of custom colors can be mixed.
